Project Code 1556

Home Control (Omni Devices)
SAP S/4HANA Cloud Project Kickoff

Alex Chua
Consulting Director
ISS Data

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsors
SAP S/4HANA Cloud Public Edition (S4HC) Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
SAP S/4HANA Cloud Public Edition (S4HC) Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
SAP S/4HANA Cloud Public Edition (S4HC) Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

SAP S/4HANA Cloud Mindset Building Blocks



Fit-to-Standard

Maximize use of pre-delivered capabilities, extend where needed to preserve or enhance business value.

Agile

Follow the agile methodology and fully embrace the agile way of working.

Continuous Innovation

Readiness to adopt continuous innovation with the release cycles.



Dynamic Extensibility & Integrations

In-app, developer, and side-by-side extensions. Open APIs on SAP API Business Hub.

Digital Transformation

Users are fully engaged with the digital transformation, are clear about the objectives and business needs.

Collaborative

Users embrace collaborative way of working as opposed to working in silos.

Continuous innovation through automated upgrades

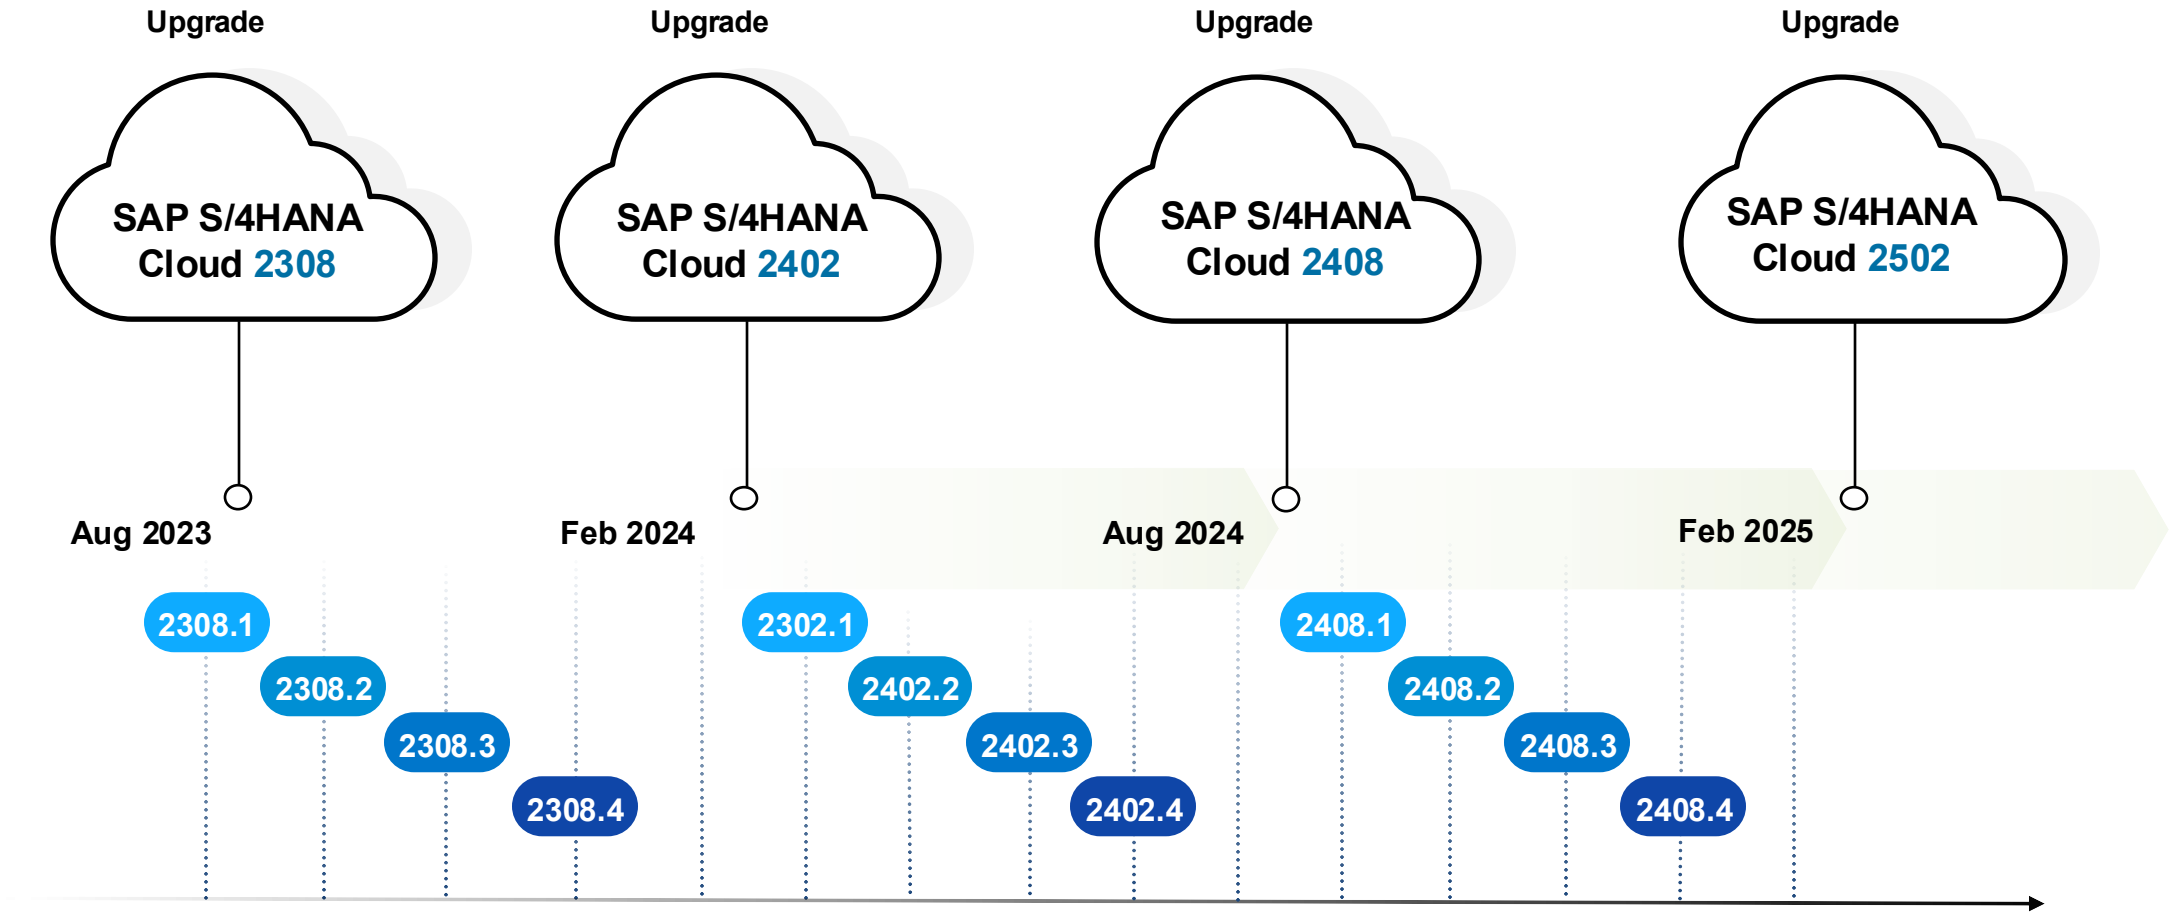

This is the current state of planning, which can be changed by SAP at any time without prior notice.

Workshop Objectives

1. **Confirm the Project Scope**
   Validate and align on the defined objectives, deliverables, and boundaries of the project.
2. **Understand the Delivery Approach**
   Review the methodology, timelines, and key milestones that will guide project execution.
3. **Review the System Landscape**
   Assess the current and target IT environments, including infrastructure, applications, and integrations.
4. **Introduce Roles and Responsibilities**
   Define and communicate the responsibilities and expectations for all key stakeholders and team members.
5. **Learn About the Enablement Approach**
   Understand the strategy for training, knowledge transfer, and user adoption.
6. **Examine Critical Success Factors**

What Does Project Success Really Mean?

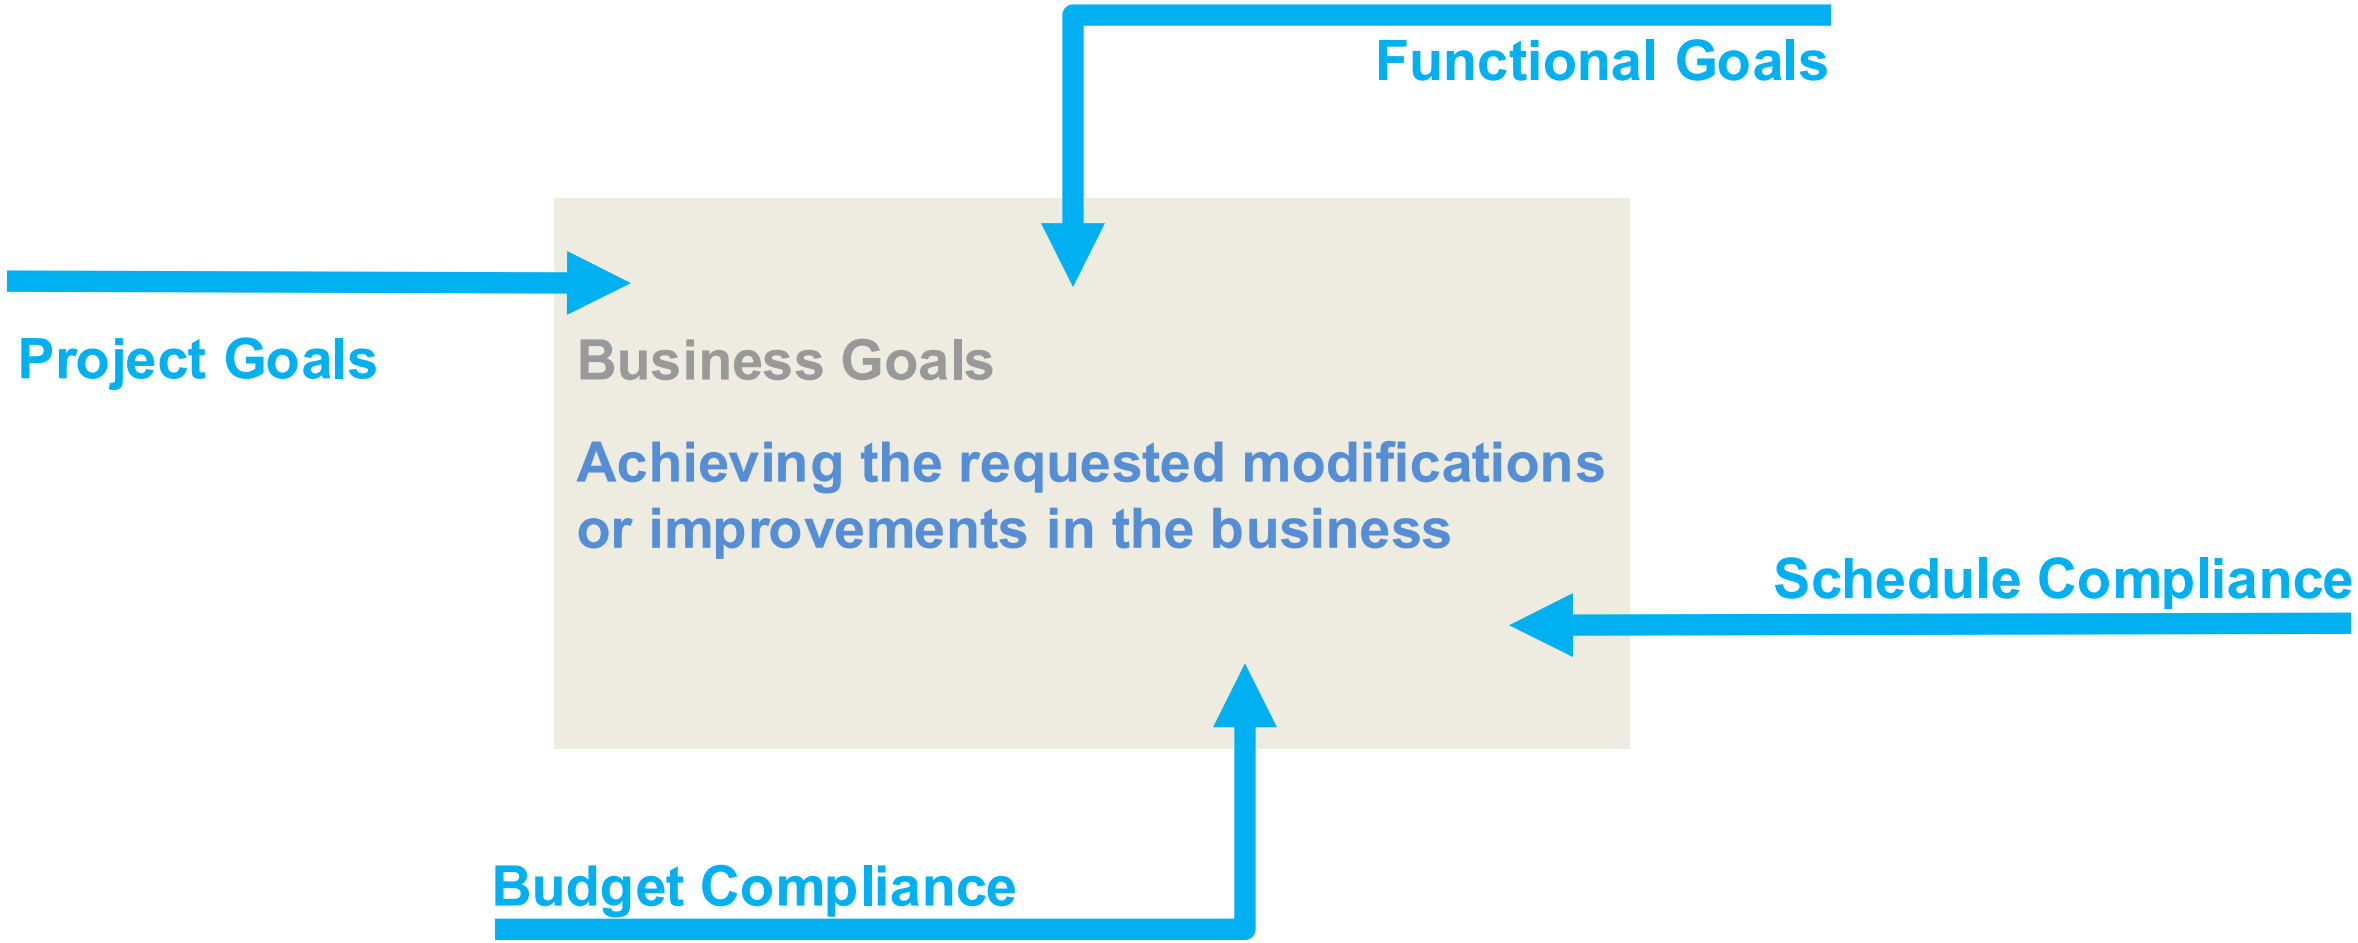

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
SAP S/4HANA Cloud Public Edition (S4HC) Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Omni Devices Expectations

Home Control 2024 (Confidential)

Omni Devices Key Objectives

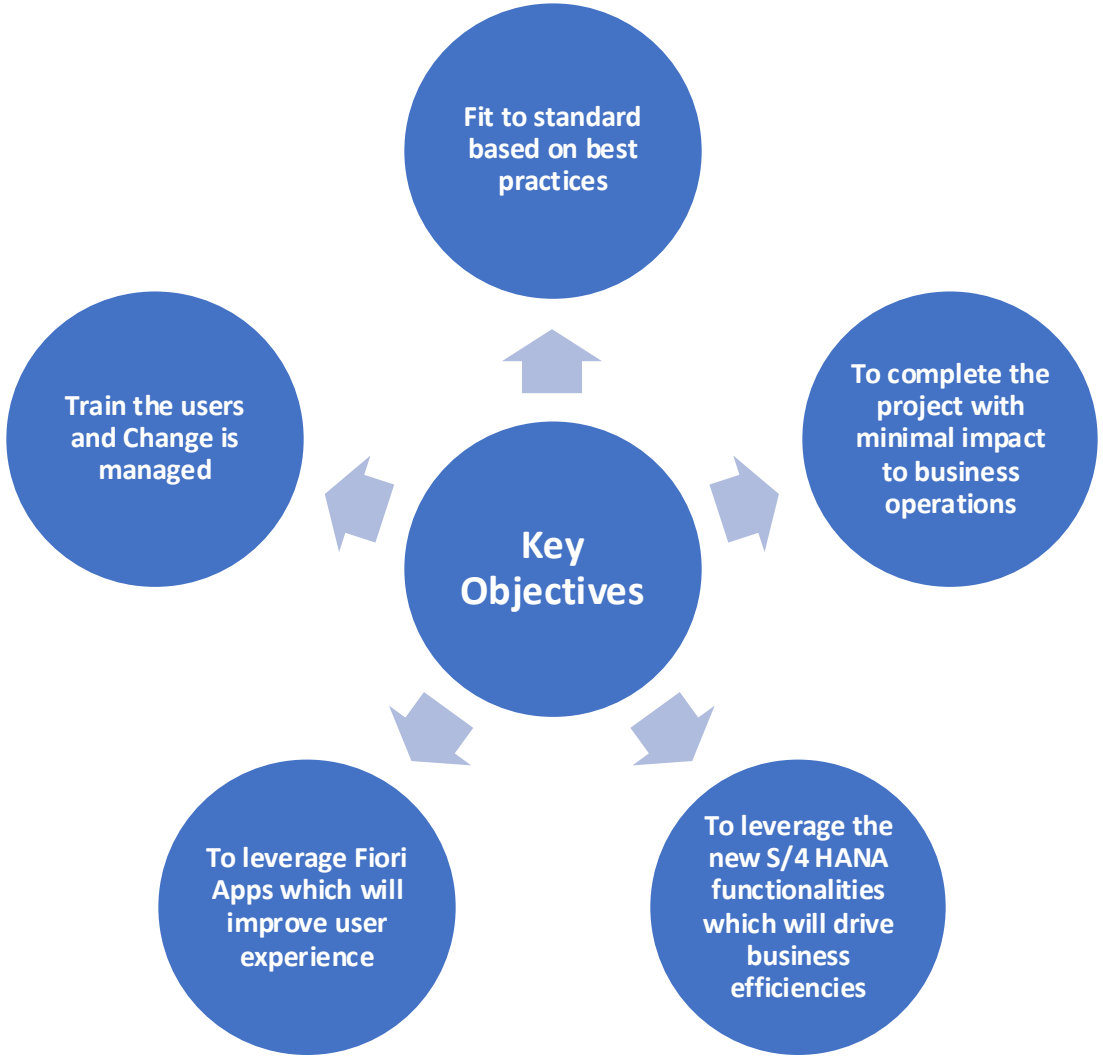

OMNI DEVICES

Business Process Improvement Requirements from Home Control

Potential changes & improvements to make with S/4 HANA (within current implemented modules):

- Monitoring Supplier inventory status
- Real time information for sales planning
- Improve forecast planning
- Automatic SO based on sales contract
- A tracked workflow for purchasing info record
- Scrap monitoring during the production process
- BoM comparison for R&D Purpose
- Freight cost allocation by product/region/customer
- Automate invoice validation and data capture
- Master data creation process
- Integration with third party system

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
S4HC Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Project Team and Roles

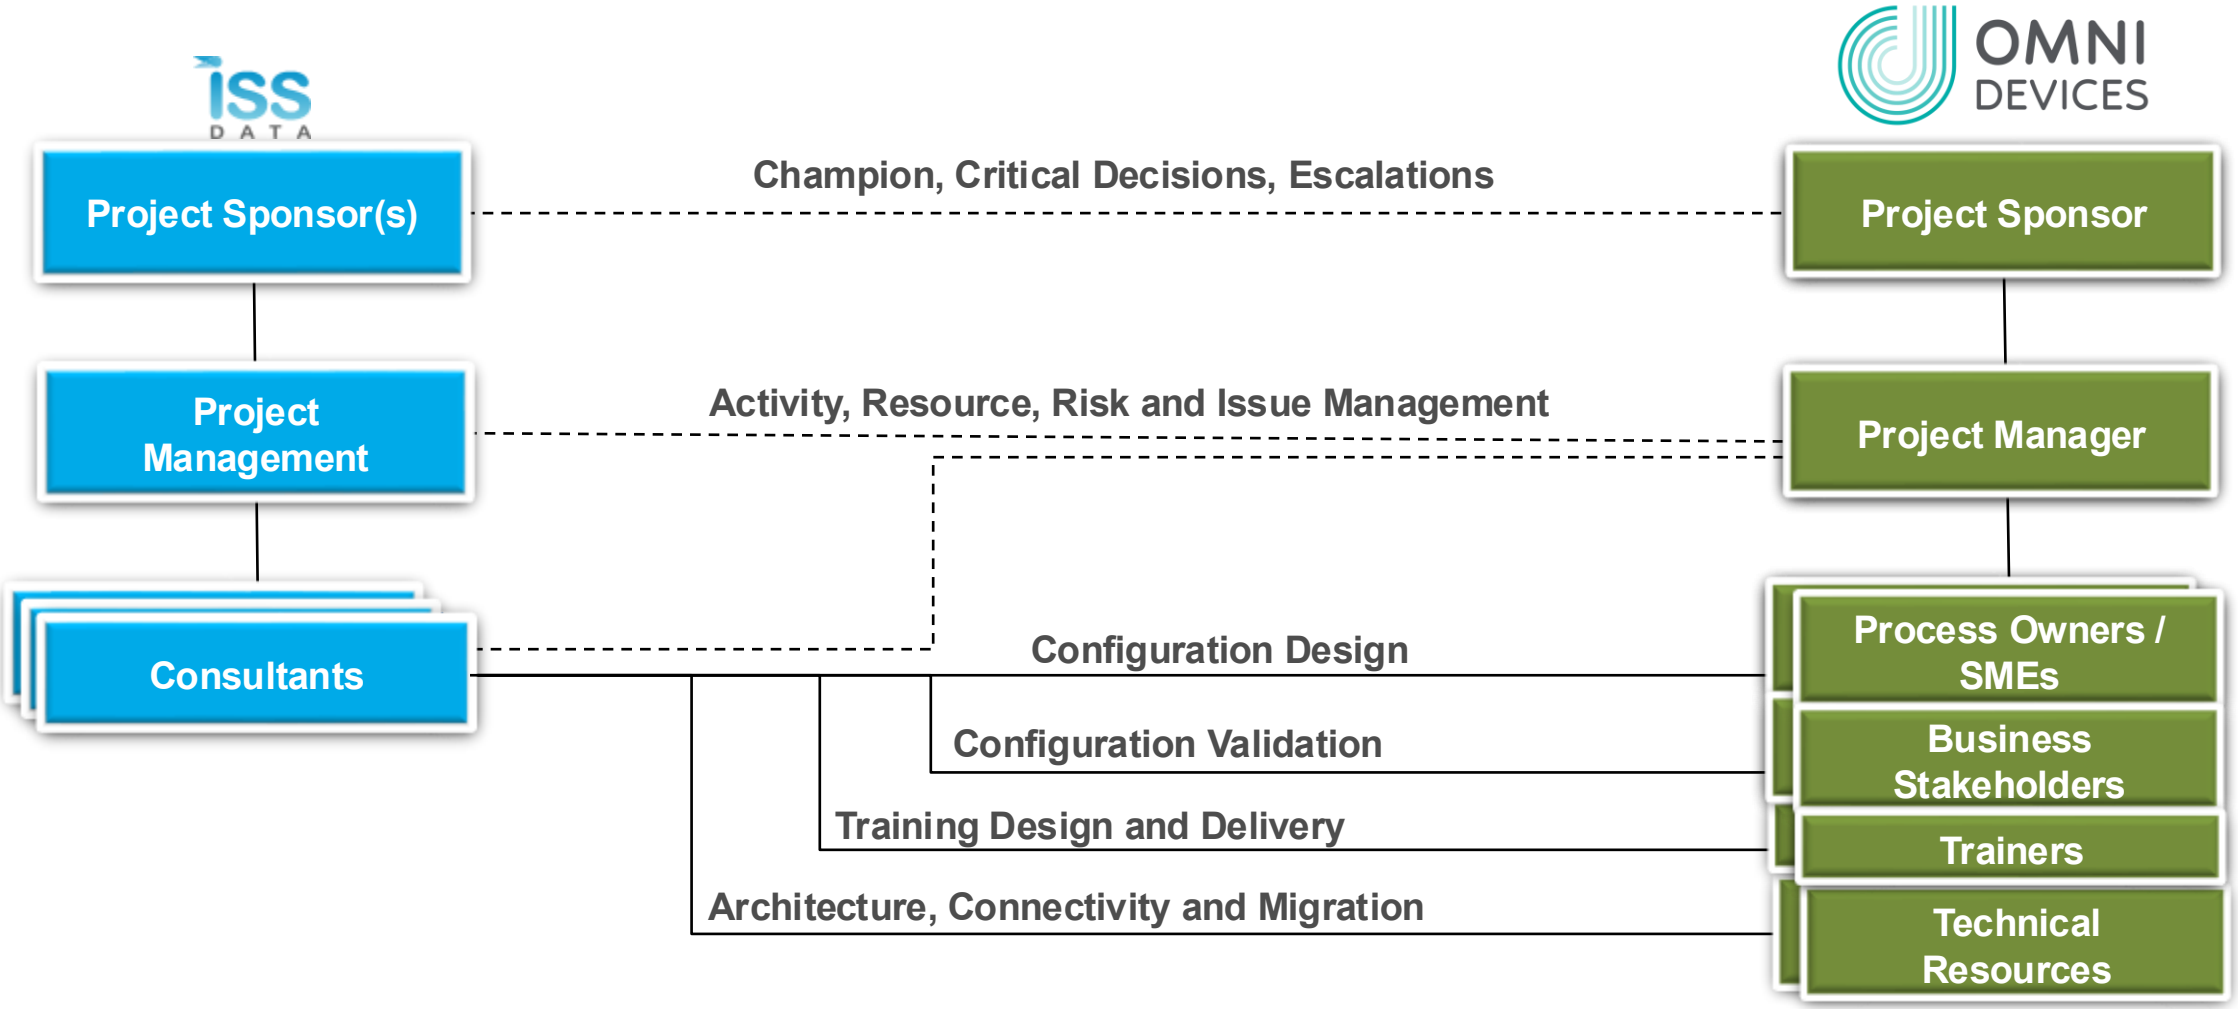

Key Implementation Roles – Home Control

Project Lead

- Owns and drives the project jointly with the Partner Project Manager
- Coordinates all aspects of the project to meet defined objectives
- Manages relationship with project stakeholders
- Manages Q-Gate processes

Business Process Expert

- Understands business and processes
- Performs and confirm configuration
- Performs testing
- Drives decisions

System Administrator

- Provides consistency across the customer's technical landscape during the solution lifecycle
- Manages interactions with the services center
- Serves as the central contact for SAP
- Responsible for receiving and requesting tenants



Configuration Expert

- Expert in solution processes and configuration
- Prepares and leads the Fit-to-Standard analysis process
- Performs/guides the system configuration
- Resolution of business process issues



Analytics Expert

- Expert in the delivered analytics content
- Creation of the overall analytics design
- Managing reporting delta requirements with various functional teams
- Developer for new and/or extended reports and data structures

Integration Implementation Expert

- Responsible for the definition and setup of integrations
- Identification and testing of needed interfaces
- Identification of scope items
- Development of setup guides for customer driven integrations
- Performs integration setup
- Supports cross system process testing

Certification

Project Lead	Business Process Expert	System Administrator	Configuration Expert	Analytics Expert	Integration Implementation Expert
S4C Onboarding	S4C Line-of-Business	S4C Onboarding	S4C Line-of-Business	S4C Onboarding	S4C Onboarding

Key Implementation Roles – Home Control

Data Migration Expert

- Responsible for the data migration of legacy systems to the new cloud system
- Identification and qualification of source data
- Cleansing of source data
- Execution of data migration into the system

Testing Expert

- Creates and manages overall test strategy
- Manage solution testing, defects, and resolution of defects
- Coordinate test cycles during the implementation
- Manage testing activities for release updates

Extensibility Expert

- Design and implement development of solution extensions on the SAP Business Technology Platform
- Translate requirements into development activities
- Develop the extensions per the requirements and the customer business processes

Output Management and Forms Expert

- Definition and enhancement of output management and forms
- Modification of forms using Adobe LiveCycle Designer
- Configuration of output management
- Setup of the Cloud Print Manager

Education Expert

- Responsible for change management
- Develop end user trainings, learning plans/content, and train the trainers
- Assure user readiness of the solution

Certification

Data Migration Expert	Testing Expert	Extensibility Expert	Output Management and Forms Expert	Education Expert
S4C Onboarding	S4C Onboarding	S4C Line-of-Business	S4C Onboarding	S4C Onboarding

Home Control Implementation team (1 of 3)

Executive Sponsor	
Rick Siu	CEO
Project Manager	
Rocky Cai	Operations
Minting Wang	FICO & SEC
Function Managers	
Jelly Ding	Purchasing
Nancy Zhang	Supply Chain Management
Jianwei Shi	FICO
Key Users - Finance	
Sally Jin	Finance/Cash Management
Jane Chen	Costing
Steyn Vantieghem	BE10 External Accountant/PEPPOL
Rebecca Chan	Group Reporting

Home Control Implementation team (2 of 3)

Key Users – Planner	
Sara Wang	Planner
Irene Liu	Planner
Key Users – Purchasing	
Xiaodong Yu	Purchasing
Cherry Qu	Purchasing
Key Users – Procurement	
Xiaoqin Zhuo	Procurement
Zhang Lin	Procurement
Deng Li	Procurement

Home Control Implementation team (3 of 3)

Key Users – Supply Chain	
Ochoa Edith	US SCM
Key Users – Logistics	
Enly Teng	Logistics
Key Users – SIOP	
Jean Ong	SIOP

Key Implementation Roles – SAP & ISS Data



Customer Success Partner

- Provide solution/release guidance
- Manage deployment success
- Provide mission-critical support
- Provides engagement review
- Delivery of quarterly scorecard



Support Agents

- Provide support for incidents reported via self-service tools, web, and phone



Implementation Partner

- Consulting & implementation services
- Implementation safeguarding delivery
- Technical expertise
- Proactive service delivery
- Key & End User Knowledge Transfer



S/4HANA Cloud Customer Care – Product Experts

- Provide guidance to the onsite implementation team (SI & customer)
- Ambassador on SAP Activate
- Analyze & Coordinate Configuration Requests
- Engage for customer feedback and reference activities
- Ensure feedback loop into development

ISS Data Implementation team

Steering Committee (SC) Responsibilities

The Steering Committee plays a pivotal role in guiding and overseeing the project. Its key responsibilities include:

1. **Strategic Direction and Governance**
   The SC is accountable for setting the overall direction of the project, ensuring alignment with organizational goals, and maintaining effective project governance.

2. **Decision-Making and Issue Resolution**
   During SC meetings, project management presents status updates and escalates critical issues requiring SC decisions. The SC facilitates timely and effective decision-making to keep the project on track.

3. **Resource Allocation**
   The SC ensures that the project is adequately resourced, providing the necessary support and commitment to achieve successful outcomes.

4. **Conflict Resolution and Escalation Management**
   As the highest escalation authority, the SC addresses and resolves conflicts or issues that cannot be settled at lower levels.

5. **Financial Oversight**
   The SC holds ultimate responsibility for cost control and budget management, including the approval and release of project funds.

Steering Committee Members

Home Control	
Rick Siu	CEO
Eunice Ng	Group Financial Controller
Barry Cheng	Global Operations Director
Rocky Cai	Project Manager
Minting Wang	Project Manager
ISS Data	
Pohlim Koo	Executive Sponsor
Alex Chua	Project Manager
Jennifer Yang	Project Manager

Key Users Responsibilities in the implementation project

Key users play a critical role in the successful implementation of SAP S/4HANA Cloud. Their responsibilities include:

1. **Providing Expert Input**
   Leverage your domain expertise to make informed business decisions and contribute to the definition and design of the solution.
2. **Executing Assigned Implementation Tasks**
   Complete all implementation-related activities as assigned, ensuring alignment with project timelines and objectives.
3. **Acting as Change Agents**
   Serve as a knowledge multiplier by training and supporting end users within your organization, fostering adoption and effective system usage.
4. **Acquiring System Configuration Skills**
   Develop a working knowledge of the system configuration relevant to your area to support ongoing improvements and troubleshooting.

Key Users Responsibilities After Go-Live

Incident Management

- Search for solutions and process incidents from end users directly and when necessary, request help from SAP

Manage Users and Task Assignment

- Deal with user authorization requests
- Maintain responsibilities for users in your company
- Resolve any unassigned business tasks

Manage Background Jobs, Input and Output

- Monitor background jobs
- Monitor internal/external communications such as printers and integration with third-parties

Knowledge Transfer

- Act as a multiplier within your organization to train and support new users of the SAP solution

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
S4HC Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Solution Scope – (1 of 8)

Area	Scenario ID	Scenario
Finance	1EG	Bank Integration with File Interface
Finance	1GI	General Ledger Allocation Cycle
Finance	1GO	Cash Journal
Finance	1HB	Financial Plan Data Upload from File
Finance	1NT	Project Control - Finance
Finance	1T6	Lease-In Accounting
Finance	1T6	Lease-In Accounting
Finance	1ZT	Managing Material Price Changes and Inventory Values
Finance	21P	Lease-In Accounting - Group Ledger IFRS
Finance	21P	Lease-In Accounting - Group Ledger IFRS
Finance	2FM	Financial Planning and Analysis
Finance	2FM	Financial Planning and Analysis
Finance	2JB	SAP Fiori Analytical Apps for Financial Accounting

Solution Scope – (2 of 8)

Area	Scenario ID	Scenario
Finance	2LH	Automated Invoice Settlement
Finance	2QL	Universal Allocation
Finance	2QY	SAP Fiori Analytical Apps for Asset Accounting in Finance
Finance	2V7	Monitoring of Goods and Invoice Receipts
Finance	5IS	VAT Tax Calculation and Reporting for Belgium
Finance	5XU	Document and Reporting Compliance
Finance	BD6	Basic Credit Management
Finance	BEG	Standard Cost Calculation
Finance	BEJ	Inventory Valuation for Year-End Closing
Finance	BFA	Basic Bank Account Management
Finance	BFB	Basic Cash Operations
Finance	BFH	Asset Under Construction
Finance	BGC	SAP Fiori Analytical Apps for G/L Accounting in Finance

Solution Scope – (3 of 8)

Area	Scenario ID	Scenario
Finance	BNA	Period-End Closing - Projects
Finance	J54	Overhead Cost Accounting
Finance	J55	Margin Analysis
Finance	J58	Accounting and Financial Close
Finance	J58	Accounting and Financial Close
Finance	J59	Accounts Receivable
Finance	J60	Accounts Payable
Finance	J62	Asset Accounting
Human Resources	1FD	Employee Integration - SAP S/4HANA Enablement
IT Management	1LQ	Output Management
Manufacturing	4B5	Predictive Material and Resource Planning
Manufacturing	BJK	Production Subcontracting - External Processing
Manufacturing	BJK	Production Subcontracting - External Processing

Solution Scope – (4 of 8)

Area	Scenario ID	Scenario
Manufacturing	BJK	Production Subcontracting - External Processing
Manufacturing	BMY	Subcontracting
Manufacturing	J44	Material Requirements Planning
Manufacturing	J44	Material Requirements Planning
R&D/Engineering	1NT	Project Control - Finance
R&D/Engineering	35F	Project Control – Capital Projects
Sales	1BS	SAP Fiori Analytical Apps for Sales
Sales	1EZ	Credit Memo Processing
Sales	1F1	Debit Memo Processing
Sales	1HO	Intercompany Sales Order Processing - Domestic
Sales	1MC	Omnichannel Convergent Billing
Sales	1MI	Delivery Processing Without Order Reference
Sales	1MX	Intercompany Sales Order Processing - International

Solution Scope – (5 of 8)

Area	Scenario ID	Scenario
Sales	1WO	Extended Intercompany Processes for Sales
Sales	2EQ	Sale of Services
Sales	2ET	Sales Order Processing for Non-Stock Material
Sales	2F4	Intercompany Process for Customer Returns
Sales	5D2	Advanced Intercompany Sales
Sales	BD9	Sell from Stock
Sales	BDA	Free of Charge Delivery
Sales	BDD	Lean Customer Returns
Sales	BDG	Sales Quotation
Sales	BDH	Sales Order Entry with One-Time Customer
Sales	BDQ	Invoice Correction Process with Debit Memo
Sales	BKA	Free Goods Processing
Sales	BKJ	Sales Order Processing with Customer Down Payment

Solution Scope – (6 of 8)

Area	Scenario ID	Scenario
Sales	BKL	Invoice Correction Process with Credit Memo
Sales	BKP	Customer Returns
Sourcing and Procurement	18J	Requisitioning
Sourcing and Procurement	18J	Requisitioning
Sourcing and Procurement	1JI	Real-Time Reporting and Monitoring for Procurement
Sourcing and Procurement	1JI	Real-Time Reporting and Monitoring for Procurement
Sourcing and Procurement	22Z	Procurement of Services
Sourcing and Procurement	22Z	Procurement of Services
Sourcing and Procurement	2LH	Automated Invoice Settlement
Sourcing and Procurement	2LH	Automated Invoice Settlement
Sourcing and Procurement	2NX	Scheduling Agreement for Subcontracting Procurement
Sourcing and Procurement	BMD	Purchase Contract
Sourcing and Procurement	BMY	Subcontracting

Solution Scope – (7 of 8)

Area	Scenario ID	Scenario
Sourcing and Procurement	BMY	Subcontracting
Sourcing and Procurement	BNX	Consumable Purchasing
Sourcing and Procurement	BNX	Consumable Purchasing
Sourcing and Procurement	J45	Procurement of Direct Materials
Sourcing and Procurement	J45	Procurement of Direct Materials
Supply Chain	2LH	Automated Invoice Settlement
Supply Chain	2LN	Basic Available-to-Promise Processing
Supply Chain	3BS	Warehouse Outbound Processing
Supply Chain	3BX	Warehouse Physical Inventory
Supply Chain	4LU	Physical Inventory - Cycle Counting
Supply Chain	6NH	Wave Management in Warehousing
Supply Chain	BMC	Core Inventory Management

Solution Scope – (8 of 8)

Area	Scenario ID	Scenario
Supply Chain	BMK	Return to Supplier
Supply Chain	BML	Physical Inventory - Inventory Count and Adjustment
Supply Chain	BMY	Subcontracting
Supply Chain	J45	Procurement of Direct Materials
App. Platf. and Infrastr.	1NJ	Responsibility Management
Database and Data Mngt.	1FD	Employee Integration - SAP S/4HANA Enablement
Database and Data Mngt.	1NJ	Responsibility Management
Database and Data Mngt.	1RK	Mass Load and Mass Maintenance for Business Partner
Database and Data Mngt.	1RM	Mass Load and Mass Maintenance for Product
Database and Data Mngt.	2Q2	Data Migration to SAP S/4HANA from Staging
Database and Data Mngt.	BH3	Data Migration to SAP S/4HANA from SAP

Solution Scope – Countries

Singapore	China (2)
USA	Brazil
Belgium	Cayman Islands

Solution Scope – Companies

Home Control Singapore Pte Ltd	Singapore
HC (Suzhou) Limited	China (Suzhou)
Home Control Solutions (Suzhou) Limited	China (Suzhou)
Premium Home Control Solutions LLC	US (El Paso)
Home Control Europe NV	Belgium (Leuven)
Home Control International Limited	GB (Cayman Island)
Omni Remote Do Brasil Ltda	Brazil

Solution Scope – Organisation Structure

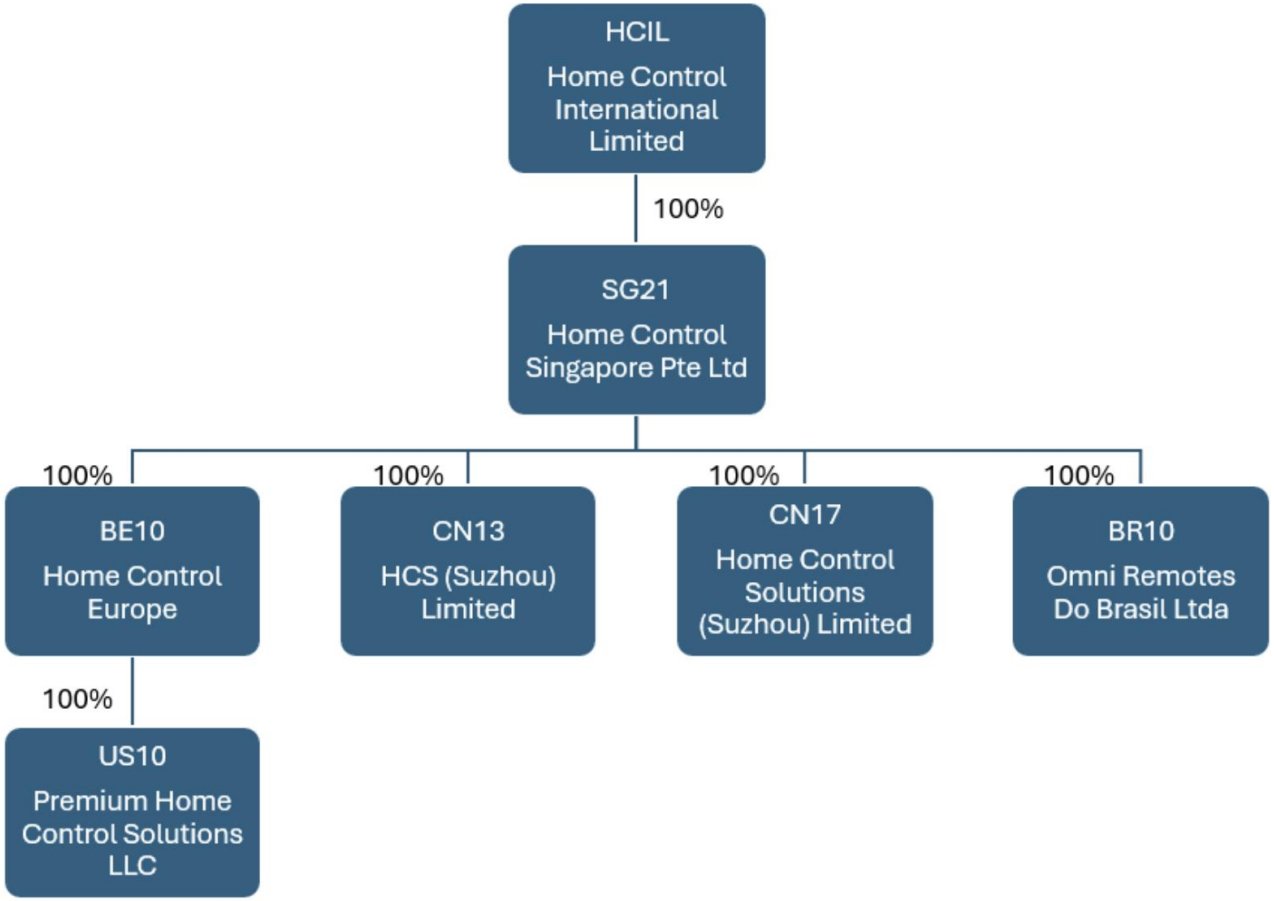

Solution Scope

Currency	In accordance with the contract
Set of Books	In accordance with the contract
System & Implementation Language	English

Integration Points in Scope

Integration Point	From Product/Solution	To Product/Solution	Data Transfer	Data Transfer
Short description of integration point			**Technical nature of integration flow**	**Longer description of scope of integration perhaps covering business objects or data**
SAP DRC	S4HC	Peppol Service Provider	Bi-directional	SAP web service will be consumed to pull the invoice data from SAP, and E-Invoice details will be pushed back to SAP
Product	S4HC	Smart Operations Systems (SOS)	Unidirectional	SOS system will consume the SAP API to query the new products created in SAP
SAP SAC	S4HC	SAC	Unidirectional	Standard Live connection used to run report

Landscape

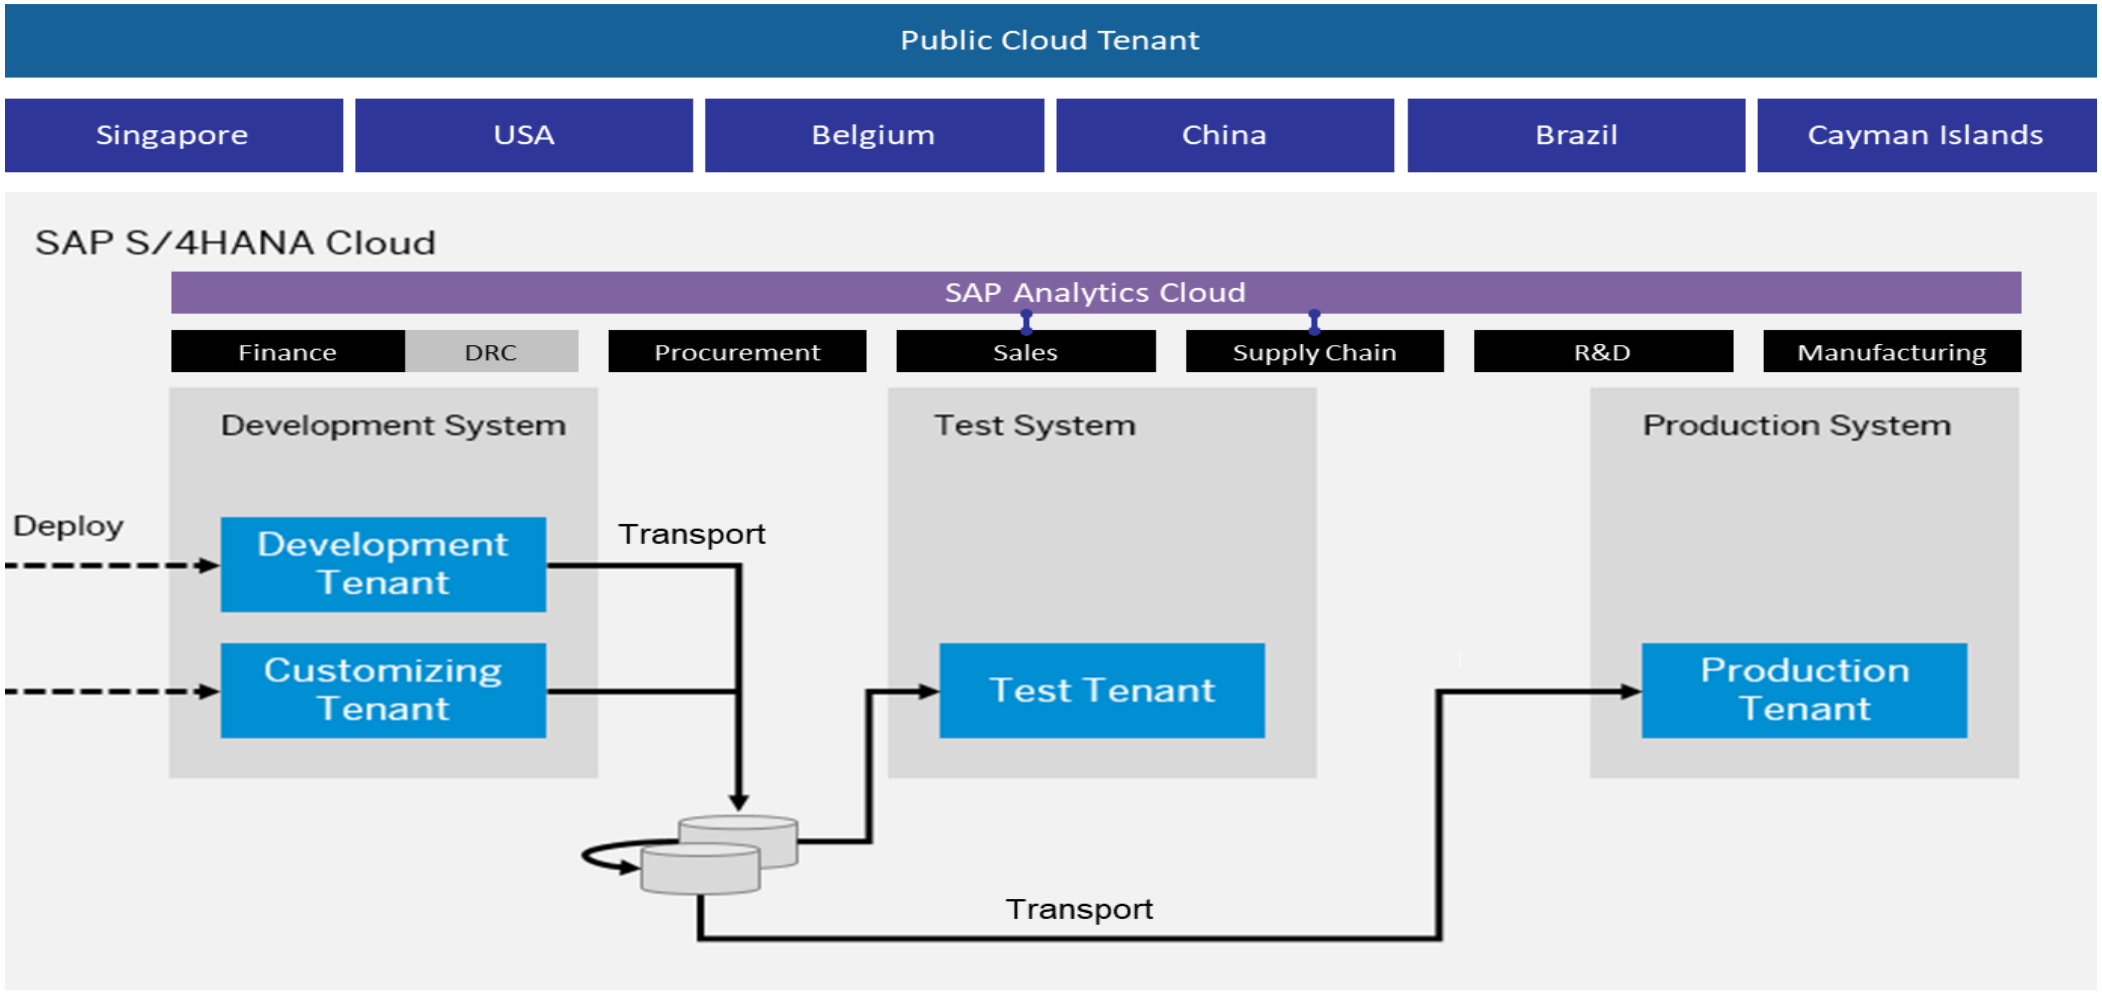

Live S4HC Connection to SAC

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
S4HC Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Deploy SAP S/4HANA Cloud with SAP Activate

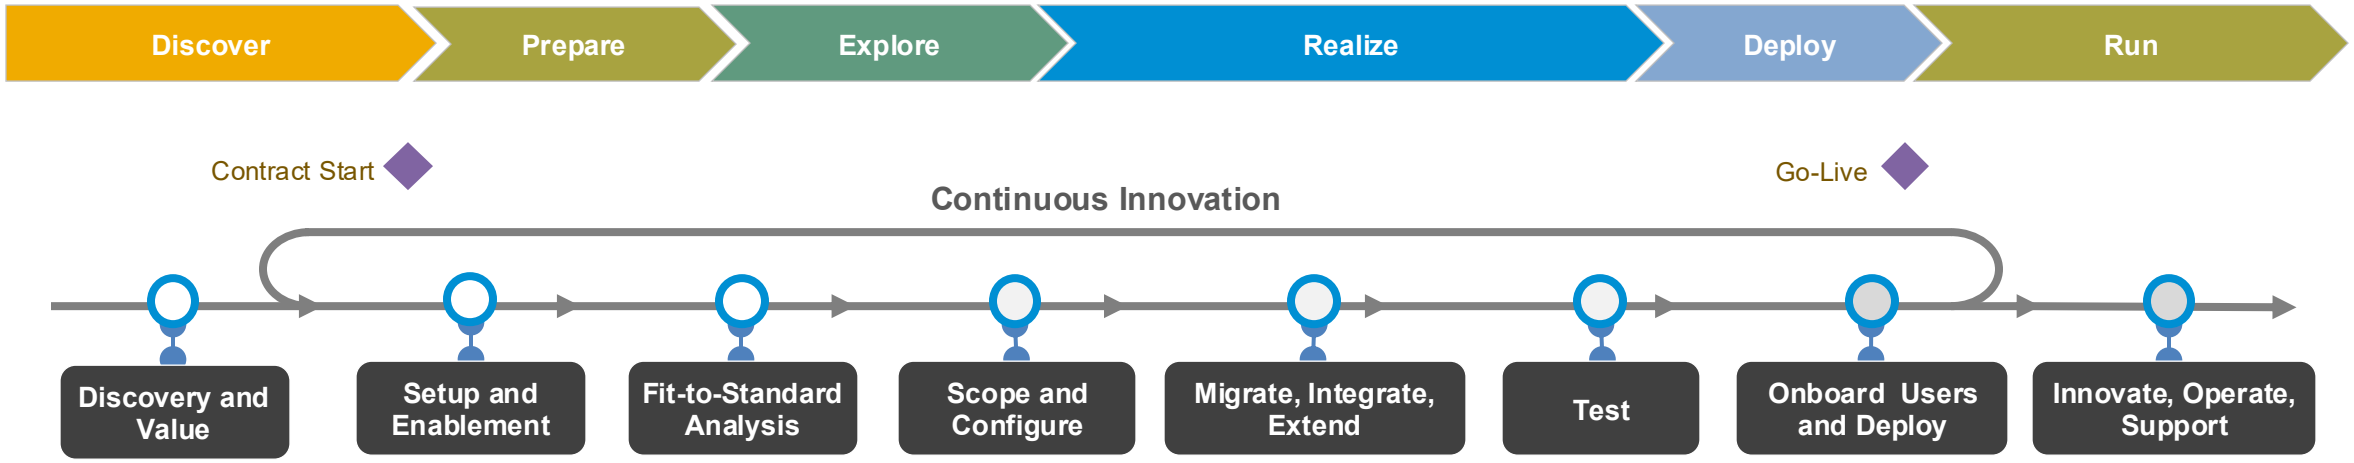

Discover the solution capabilities, understand the business value and benefits of the solution to customer's business.

Initial planning and preparation of the project. Onboard and enable project team. Provision initial landscape and ALM tools.

Run a fit-to-standard analysis, validate the solution fit, and identify delta requirements for config, data, integration and extensibility.

Perform a series of agile iterations to configure, extend and test an integrated business environment. Perform data loads, adoption activities, and plan production operations.

Finalize setup of the production landscape, data loads, confirm readiness, and go-live with the new solution.

Continue adoption of the solution across the business. Do regression test for system upgrades. Activate additional functionality as needed.

Project Plan & Tasks

06 Jun – 27 Jun (2W)	30 Jun – 08 Aug (6W)	11 Aug – 17 Oct (10W)	20 Oct – 30 Nov (5W)
Prepare	**Explore**	**Realize**	**Deploy**
Prepare Project	Execution/Monitoring of Project	Execution/Monitoring of Project	Execution/Monitoring of Project
Execution/Monitoring of Projects	*End User Learning Needs Analysis and Plan*	Quality System Initial Access	*End User Learning*
Getting Started with the Implementation of SAP S/4HANA Cloud	*Organizational Change Management Impact Analysis*	*Production System Request*	*OCM Execution Activities*
Starter System Initial Access	**Fit-to-Standard Analysis**	*Production System Initial Access*	Production Cutover
Project Initiation and Governance	*Customer Execution of Standard Processes*	*OCM Alignment activities*	*System Go Live*
Project Standards & Infrastructure	*Data Mapping*	Required Configuration Before System Use	Production Support After Go Live
Project Plans, Schedule and Budget	**Solution Definition**	*User Access and Security*	Phase Closure and Sign-Off Phase Deliverables
SAP Supporting Implementation Tools Access	*Data Load Preparation*	*Legacy Data Migration*	
Customer Team Self-Enablement	*Quality System Request*	Solution Configuration	
Organizational Change Management Roadmap	Test Planning	*Output Management Setup*	
Project Kick-Off and On-Boarding	*Learning Team*	*Learning Content*	
Fit-to Standard Analysis Preparation	Phase Closure and Sign-Off Phase Deliverables	*Test Preparation*	
Fit-to Standard System Preparation		*Test Execution*	
End User Learning Strategy		*Solution Walkthrough*	
Data Migration Approach and Strategy		*Cutover Plan*	
Business Driven Configuration Assessment		*Technical Operations & Handover Plan*	
Phase Closure and Sign-Off Phase Deliverables		Phase Closure and Sign-Off Phase Deliverables	

- *Customer*
- ISS Data
- Collaborative

SAP Activate Methodology – Prepare Phase

Prepare | Explore | Realize | Deploy

- Project Initiation / Governance
- Project Kickoff / On-boarding
- System Access
- Customer Team Self-Enablement
- Business Driven Configuration Assessment
- User Learning Plan
- Data Migration Plan
- Integration and Extensibility Plan

The purpose of **Prepare** phase is to provide the initial planning and preparation for the project. In this phase, the project is started, plans are finalized, project team is assigned, and work is under way to start the project optimally.

SAP Activate Methodology – Explore Phase

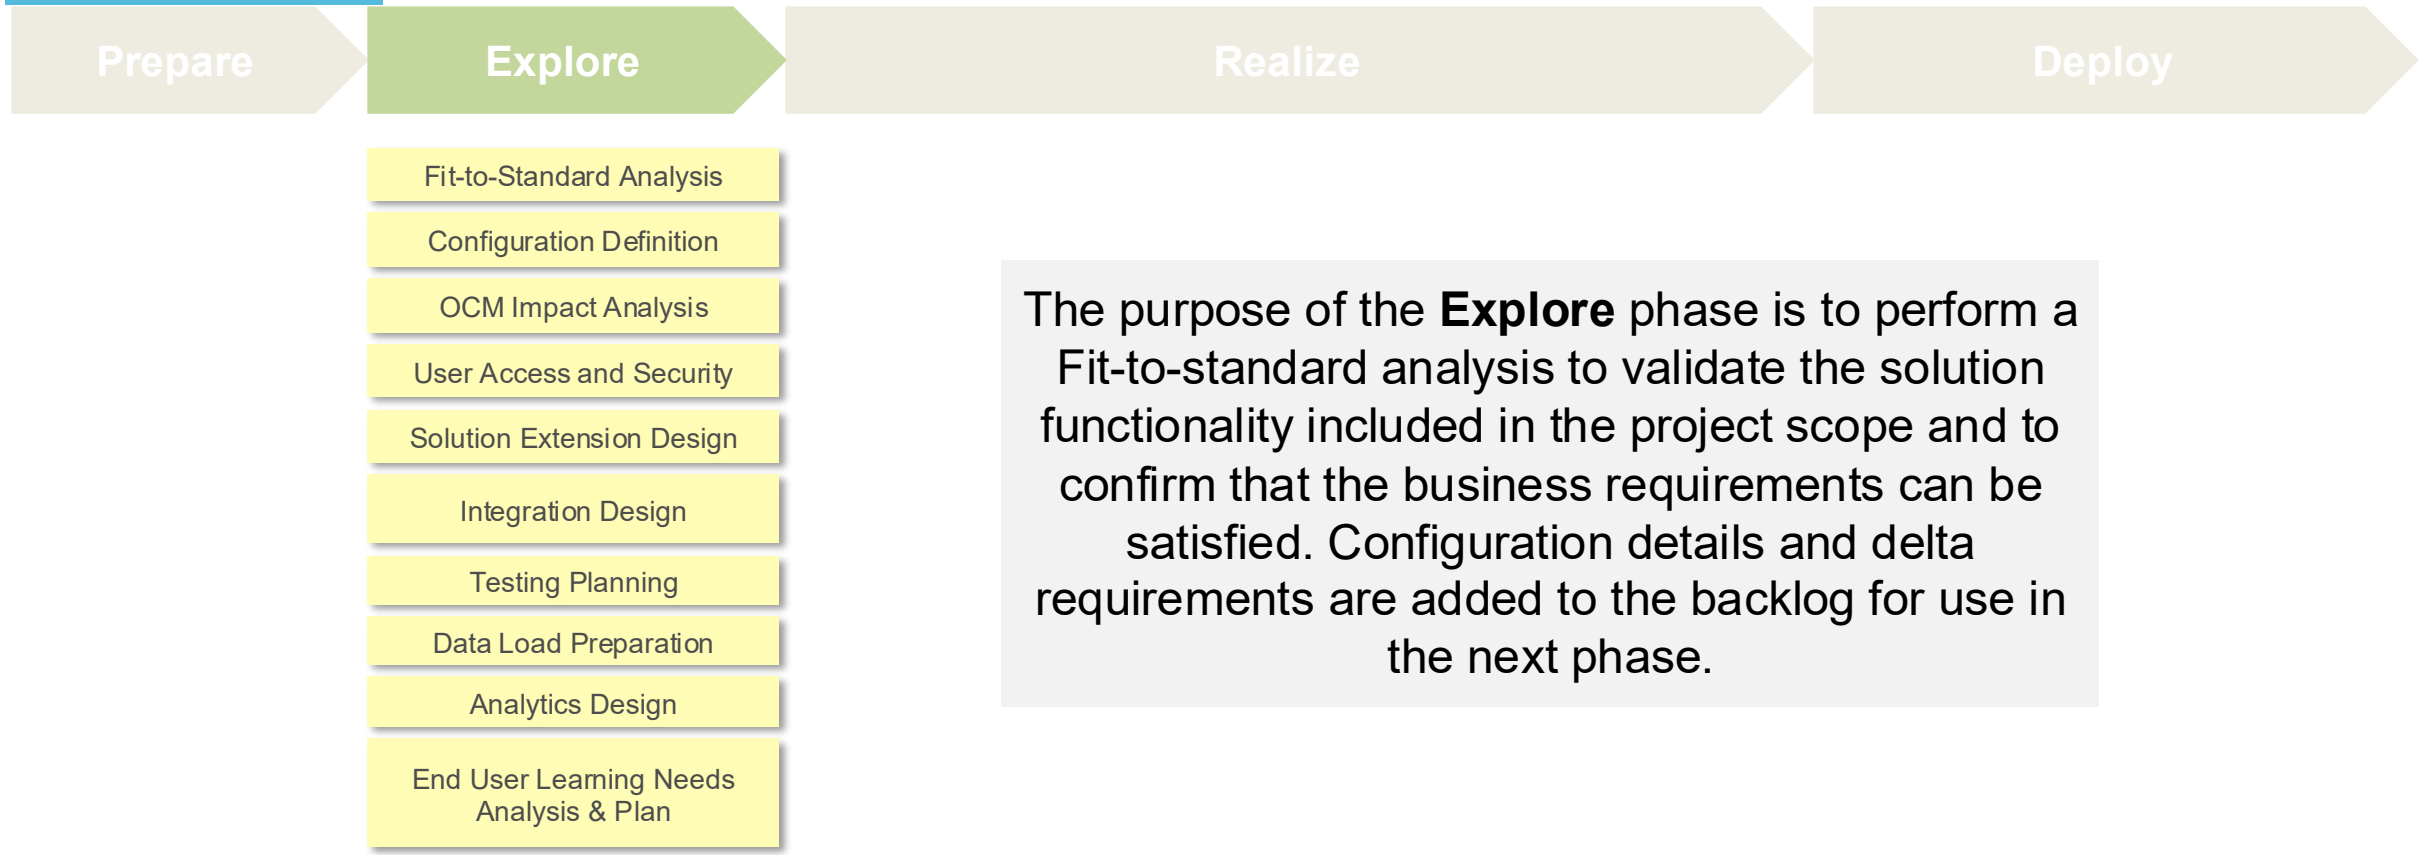

The purpose of the **Explore** phase is to perform a Fit-to-standard analysis to validate the solution functionality included in the project scope and to confirm that the business requirements can be satisfied. Configuration details and delta requirements are added to the backlog for use in the next phase.

SAP Activate Methodology – Realize Phase

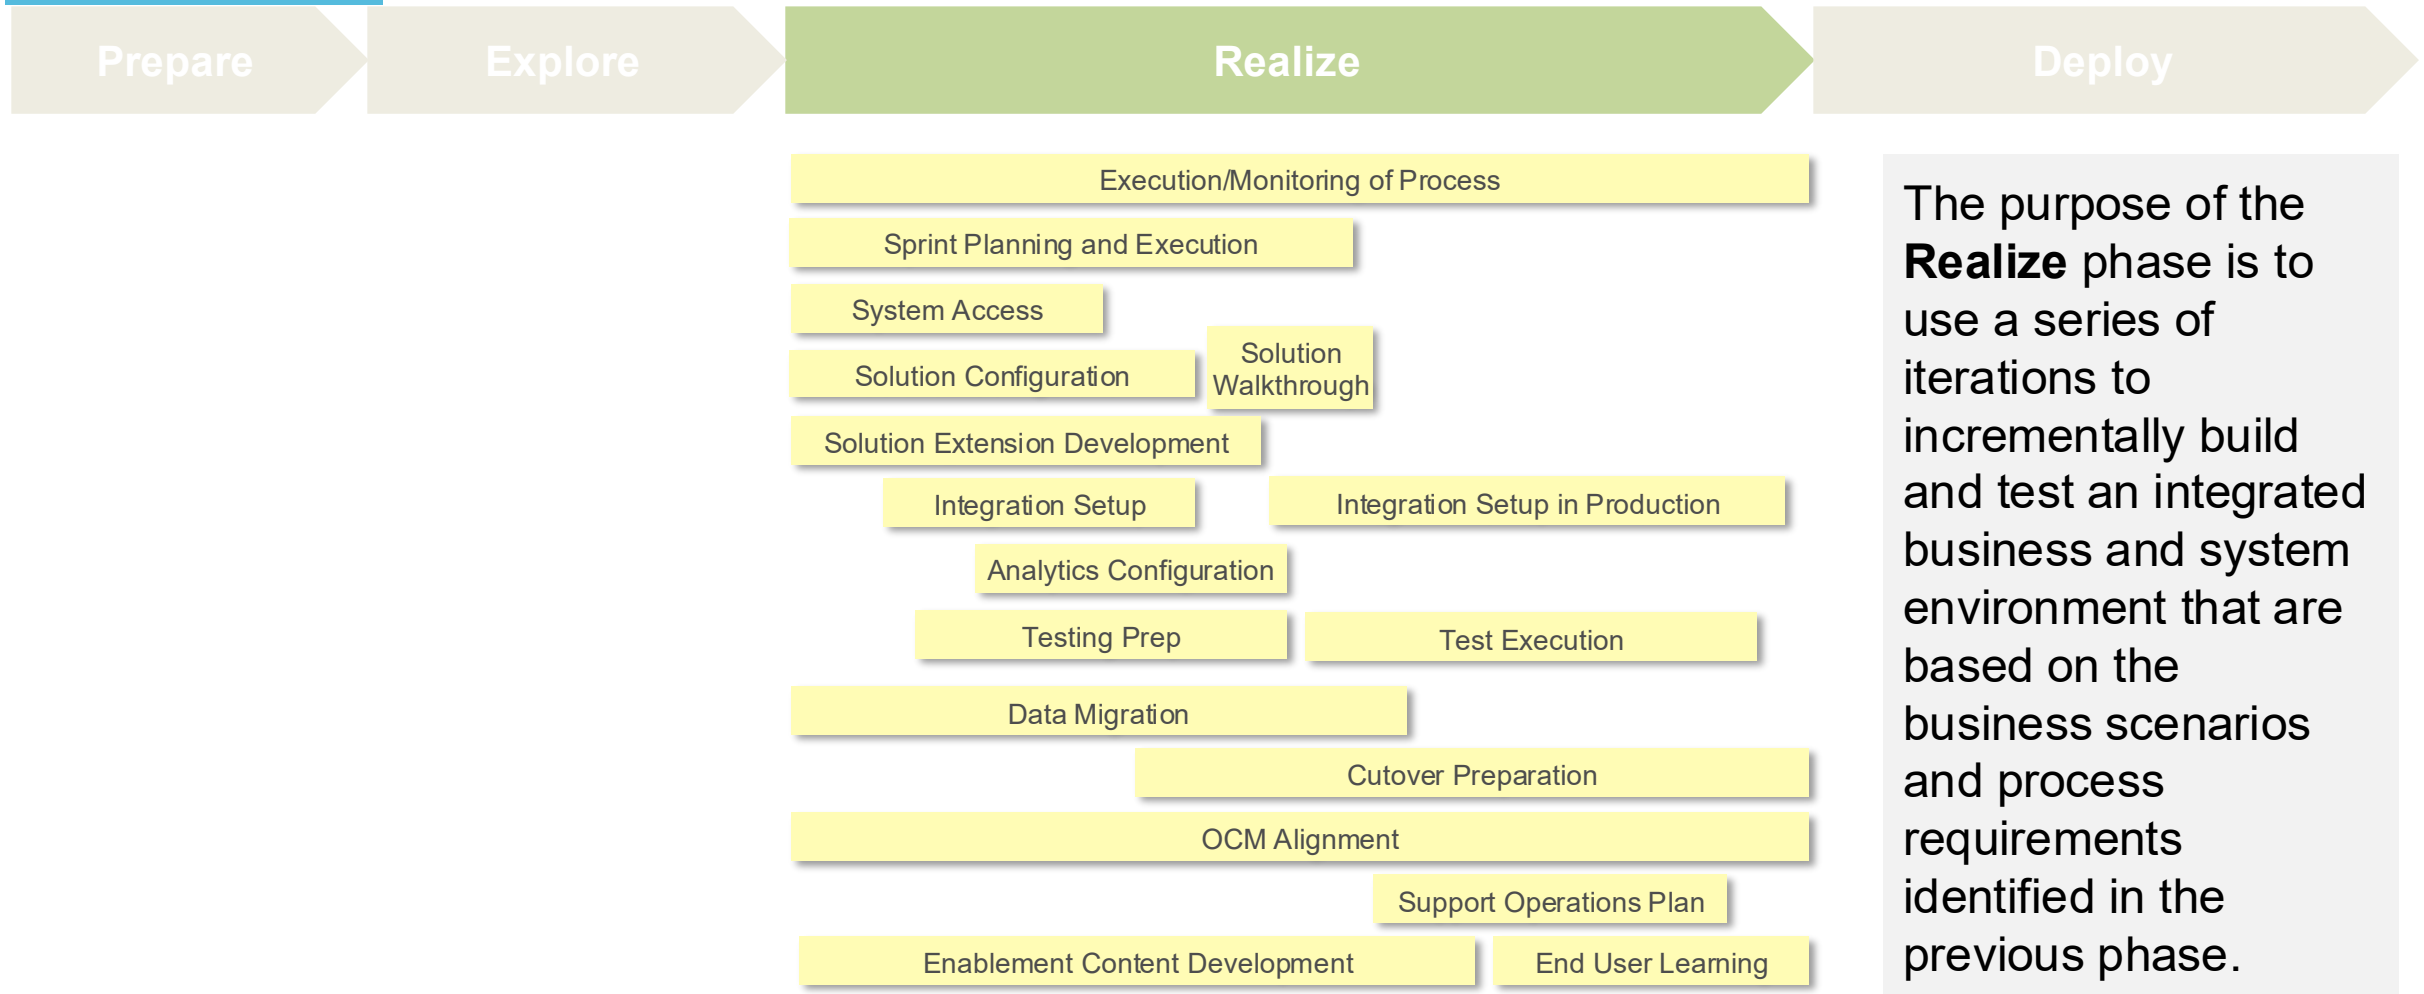

The purpose of the **Realize** phase is to use a series of iterations to incrementally build and test an integrated business and system environment that are based on the business scenarios and process requirements identified in the previous phase.

SAP Activate Methodology – Deploy Phase

Prepare | Explore | Realize | **Deploy**

- Execution/Monitoring of Process
- Production Cutover
- Extension Deployment
- OCM Execution
- Operational Readiness
- System Go Live
- Close Project

The purpose of the **Deploy** phase is to finish setup of the Production System before go-live, confirm customer organization readiness, and to switch business operations to the new cloud system.

The customer should complete execution the new cloud system learning plan to optimize user adoption. It is recommended to use a blended approach to learning and performance support for end-users. Micro-learning, social and collaborative learning, classroom or virtual instructor led delivery, and on-the-job support in person.

Testing Approach

- Unit Testing – Performed by Configurator – Performed in Development Landscape
- Integration Testing – Performed by the Customer – Performed in Quality Assurance Landscape
- User Acceptance Testing – Performed by the Customer – Performed in Quality Assurance Landscape
  - Who and When will Test Plans and Scripts be written?
  - Who will participate in Testing from the Customer?
  - How long should User Acceptance Testing last?

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
S4HC Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Critical Success Factors

Stay within the agreed scope

- Scope changes will likely impact the project timeline, your required effort and consulting costs

Have a pragmatic mindset

- Adjust your processes to fit the standard system functionality in order to simplify future upgrades and scope expansion.
- It doesn't have to be perfect. You can always improve a solution later.

Make quick decisions

- The quicker you can make decisions, the quicker your project will be able to proceed into the right direction.

Involve stakeholders early

- Identify and involve your stakeholder early - executives, employees, labor unions, key customers,…

As a key user, actively contribute to the project

- The better you represent your business area, the better the SAP cloud solution will support your processes.
- Work with your manager to secure sufficient availability for the project.

Start preparing data early

- Start cleansing your data as soon as possible to prevent project issues and delays.

Never cut corners on testing

- Only thorough testing will result in a successful go-live and stable system.

Agenda

Topic	Presenter
Introduction and Welcome	Executive Sponsor
S4HC Introduction	ISS Project Manager
Home Control Presentation	Home Control Project Manager
Team Roles and Responsibilities	ISS Project Manager
Solution Scope	ISS Project Manager
Delivery Approach	ISS Project Manager
Critical Success Factors and Communication	ISS Project Manager
Q&A + Next Steps	All

Thank You

ISS Data Pte Ltd
9 Tampines Grande
Asia Green #02-11
Singapore 528735

www.iss-data.com

DISCLAIMER
The contents of this document shall remain the confidential property of ISS Data Pte Ltd ("ISS") and may not be reproduced, distributed or communicated in whole or in part to any other party without the prior written consent of ISS. The purpose of this document is solely for the evaluation by the intended recipient. All costs and timelines provided in this document are strictly estimates and are subject to confirmation prior to acceptance of award by ISS. ISS warrants to the best of its knowledge, all reasonable care has been taken in the preparation of this document and believe the contents to be true as at the date of this document. Any services to be provided by ISS as proposed in this document shall be subject to the standard terms and conditions of ISS Master Consulting Services Agreement for the provision of the relevant services.
